

# TASK 8: Burnup Chart — 4-Sprint Localization Project (200 Story Points)

Bepha Tools E-Commerce Project

Written by Brian McCarthy

## STEP 1: DETERMINE AVERAGE VELOCITY FROM HISTORICAL DATA

**Sprint 1 velocity:** 50 story points completed

**Sprint 2 velocity:** 60 story points completed

**Sprint 3 velocity:** 40 story points completed

**Average velocity calculation:**  $(50 + 60 + 40) \div 3 = 150 \div 3 = 50$  story points per Sprint

## STEP 2: TOTAL SCOPE AND SPRINT ALLOCATION

**Total project scope:** 200 story points

**Scope breakdown:** 65 SP (Multi-Language) + 55 SP (Multi-Currency) + 80 SP (Technical Interdependencies) = 200 SP

**Sprints required:**  $200 \text{ SP} \div 50 \text{ SP average velocity} = 4$  Sprints to complete full scope

## STEP 3: CUMULATIVE PROGRESS PER SPRINT

**Start (before Sprint 1):** 0 story points completed — 200 SP remaining

**End of Sprint 1:**  $0 + 50 = 50$  story points completed (25% of total scope)

**End of Sprint 2:**  $50 + 50 = 100$  story points completed (50% of total scope)


**End of Sprint 3:**  $100 + 50 = 150$  story points completed (75% of total scope)

**End of Sprint 4:**  $150 + 50 = 200$  story points completed (100% of total scope — PROJECT COMPLETE)

| Sprint Milestone | SP Completed This Sprint | Cumulative SP Completed | Total Scope (SP) | Percent Complete | Sprint Focus                                                                                        |
|------------------|--------------------------|-------------------------|------------------|------------------|-----------------------------------------------------------------------------------------------------|
| Start            | 0                        | 0                       | 200              | 0%               | Project kick-off                                                                                    |
| End of Sprint 1  | 50 SP                    | 50 SP                   | 200 SP           | 25%              | Multi-Language: Japanese + Italian; Multi-Currency: KRW + INR; Infrastructure setup                 |
| End of Sprint 2  | 50 SP                    | 100 SP                  | 200 SP           | 50%              | Multi-Language: German + Portuguese; Multi-Currency: BRL + MXN; Technical interdependencies batch 1 |

| Sprint Milestone | SP Completed This Sprint | Cumulative SP Completed | Total Scope (SP) | Percent Complete | Sprint Focus                                                                                                 |
|------------------|--------------------------|-------------------------|------------------|------------------|--------------------------------------------------------------------------------------------------------------|
| End of Sprint 3  | 50 SP                    | 150 SP                  | 200 SP           | 75%              | Multi-Language: Chinese + Korean; Multi-Currency: ZAR + RUB + CNY + JPY; Technical interdependencies batch 2 |
| End of Sprint 4  | 50 SP                    | 200 SP                  | 200 SP           | 100%             | Final integration, performance testing, documentation review, stakeholder sign-off                           |

**BURNUP CHART: Cumulative Story Points Completed vs. Total Scope Over 4 Sprints**

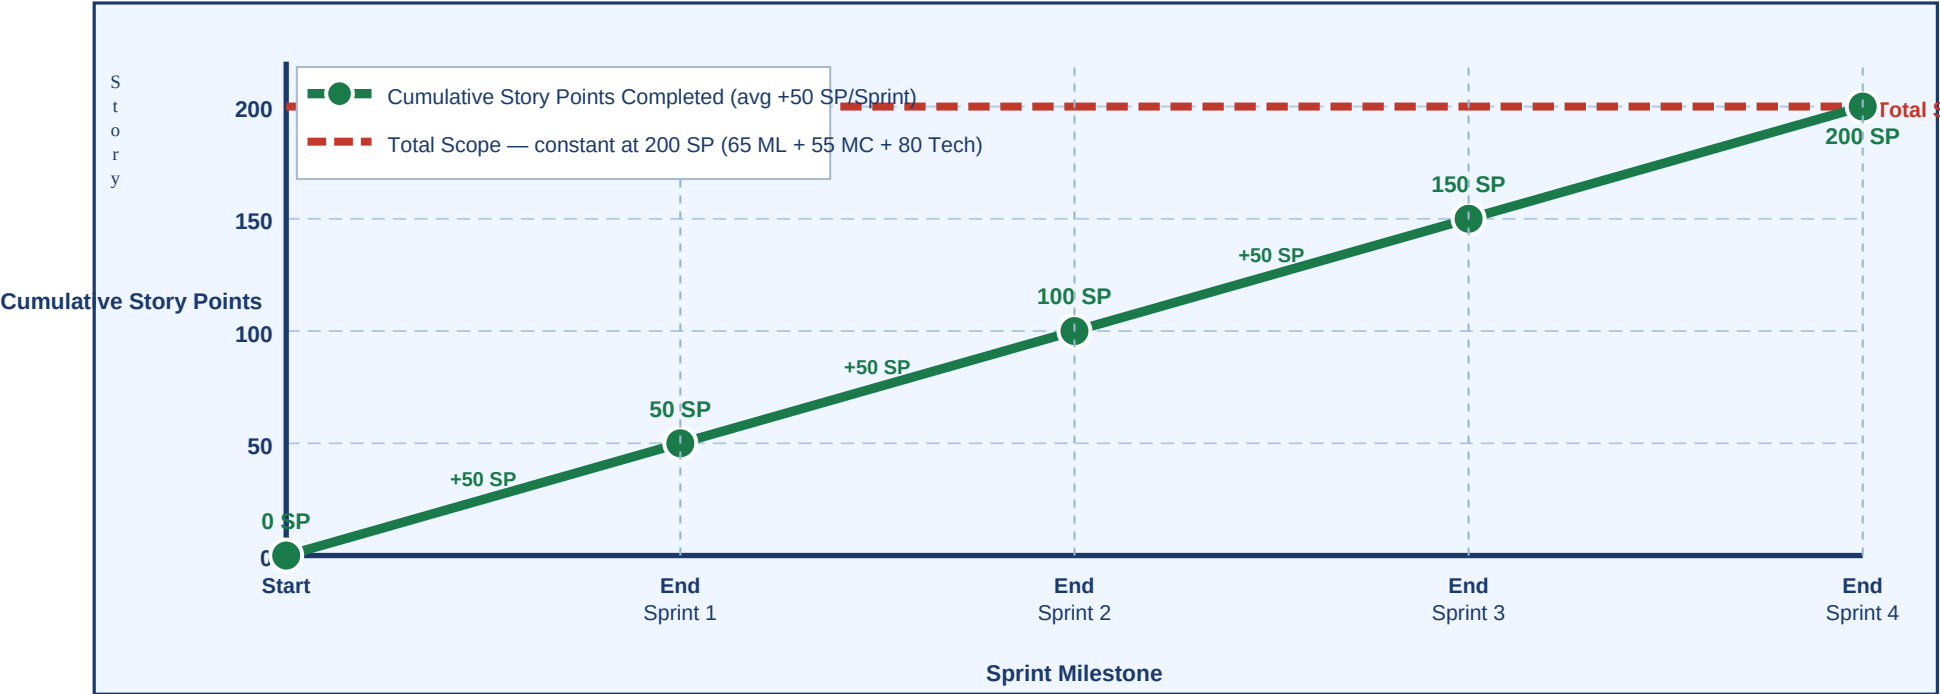

**Reading the chart:** The SOLID GREEN LINE shows cumulative story points completed, rising from 0 to 200 SP at a rate of +50 SP per Sprint (the team's average velocity). The DASHED RED LINE shows total scope — constant at 200 SP throughout the project. The two lines meet at the end of Sprint 4, confirming 100% of scope is delivered. Each '+50 SP' label on the green line indicates one Sprint's contribution at average velocity.
